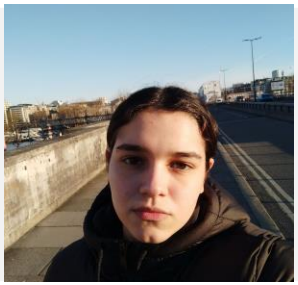
ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

LAPR3 2025/2026

[Logistics On Rails] - **SPRINT 1**

G051

Sofia Carvalho (1240898)	Mariana Moreira (1240905)	Leonor Moura (1240914)	Francisco Sá (1241341)
			

Sprint planning – Sprint 1

Planned Start Date: September 29th

Planned End Date: October 19th

Real Start Date: October 2nd

Real End Date: October 25th

SPRINT BACKLOG		
Number of stories	15	
Number of bugs	0	
Number of tasks	27	
Number of Management Tasks (Scrum)	16	
Number of team members	Planned:5	Actual:5
Total planned estimation vs execution	Planned hours: 142 Executed hours: 152	


Sprint 1 planning

Assigned User Stories (as stated in the project assignment)	Commited? Yes / No (according to team planning)	Todo	Doing	Testing	Done	Blocked
USBD01	Yes				x	
USBD02	Yes				x	
USBD03	Yes				x	
USBD04	Yes				x	
USBD07	Yes				x	
USBD12	Yes				x	
USBD18	Yes				x	


Sprint 1 planning

Assigned User Stories (as stated in the project assignment)	Commited? Yes / No (according to team planning)	Todo	Doing	Testing	Done	Blocked
USEI01	Yes				x	
USEI02	Yes				x	
USEI03	Yes				x	
USEI04	Yes				x	
USEI05	Yes				x	
USLP01	Yes				x	
USLP02	Yes				x	
USLP03	Yes				x	

Work assigned by team member

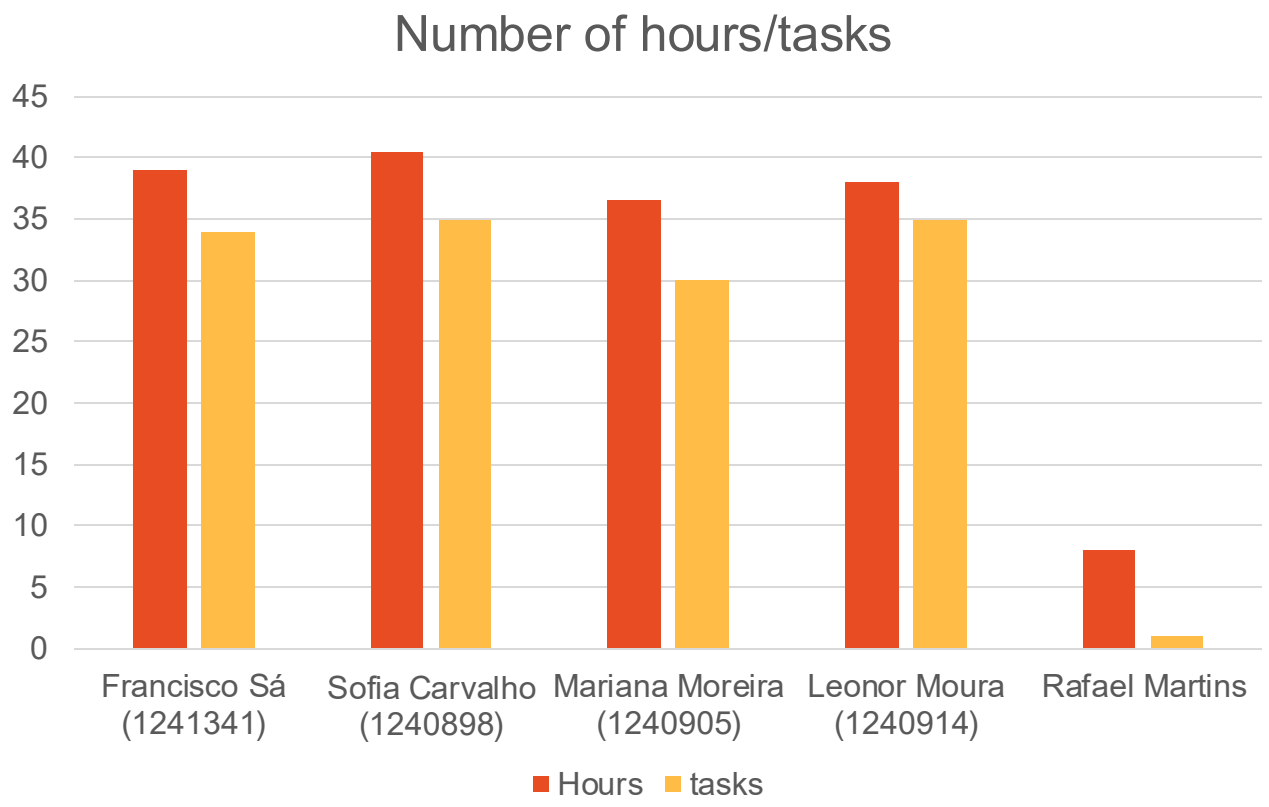

Work assigned by type (componente)

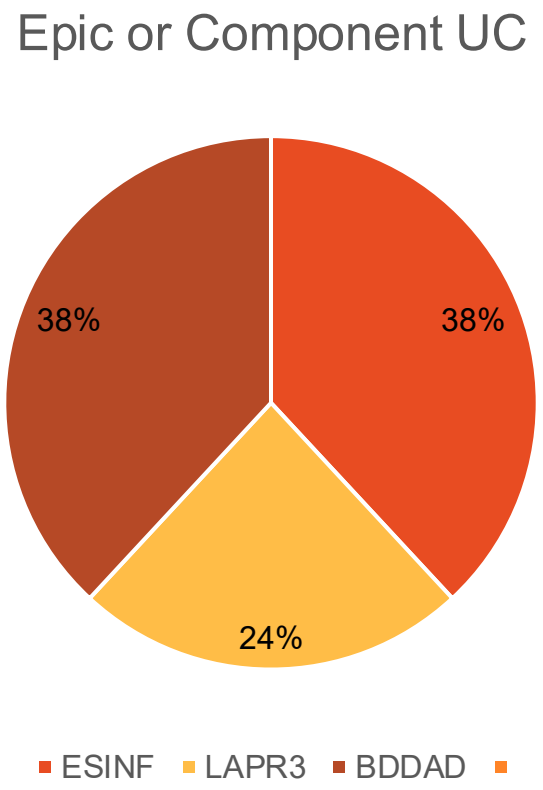

Issues / Assumptions / unanswered questions

Description	Responsible	Date / sprint	Related issue / item in Git
For the user story USLP03 - As a Traffic Dispatcher, I want to calculate the estimated travel time between two stations, with a direct connection between them, and a selected locomotive, it was not explicitly specified whether the implementation should be done in SQL or Java. We reached out to the PLs and the client for clarification, but they either did not know the answer or did not respond. To ensure the feature was delivered without blocking, we implemented the solution in both SQL and Java.	ALL	SPRINT 1	#24

Daily Meetings

Date (of the meeting)	Place / duration	Team member 1	Team member 2	Team member 3	Team member 4
02/10/2025	Class / 15 min	x	x	x	x
03/10/2025	Class / 15 min	x	x	x	x
06/10/2025	Class / 15 min	x	x	x	x
07/10/2025	Class / 15 min	x	x	x	x
08/10/2025	Class / 15 min	x	x	x	x
09/10/2025	Class / 15 min	x	x	x	x
10/10/2025	Class / 15 min	x	x	x	x
13/10/2025	Class / 15 min	x	x	x	x
14/10/2025	Class / 15 min	x	x	x	x
15/10/2025	Class / 15 min	x	x	x	x
16/10/2025	Class / 15 min	x	x	x	x

Daily Meetings

Date (of the meeting)	Place / duration	Team member 1	Team member 2	Team member 3	Team member 4
17/10/2025	Class / 15 min	x	x	x	x
21/10/2025	Class / 15 min	x	x	x	x
22/10/2025	Class / 15 min	x	x	x	x

LLM performance assessment (use ChatGPT or Copilot)

Source file (attach the file you have used):
The file is stored on the repository, following this path
sem-3-pi-25-26-g051-repo/Project/Scrum/SprintReview/Team Performance.pdf

Input (write down the prompt you used to ask for the performance assessment) :
- Let me know what you think about my team's performance in this review. You can find each team member's time/task schedule here for more effective feedback.

LLM performance assessment - Output

Output file (attach the complete file extracted from the A.I. tool):
https://chatgpt.com/share/68fea4b5-6aec-8001-aae5-1a00cb16664b

Output (write one line per team member):

Francisco Sá (1241341) - Consistency and testing — Consistent contributor across glossary, domain model, and file validation testing. Focused on ESINF US implementation and review.
Sofia Carvalho (1240898) - Documentation and structure – Managed the glossary and domain model updates, later contributed with testing and ESINF tasks. Demonstrated adaptability and good organization.
Leonor Moura (1240914) - Leadership and technical depth— Took initiative in ESINF domain setup, file validation, and later authentication and BDDAD conceptual modeling. Maintained strong leadership and technical contribution.
Mariana Moreira (1240905) - Persistence and adaptability – Actively supported glossary and domain model migration to Visual Paradigm, and later contributed to ESINF and BDDAD refinement. Persistent when facing technical issues.

LLM performance assessment - Output

Team Members' Opinion about the A.I. output:

Francisco - The AI output is almost right, I think we had a well balanced sprint except for Rafael's part because he only has ESINF (which is normal).

Sofia - Overall, I believe the work distribution and performance across the team were very balanced, with everyone contributing consistently and maintaining a similar level of effort and productivity.

Leonor – I think that the AI is overall right, the team performed very well. The work distribution was balanced, and I believe that everybody contributed to the success of this sprint.

Mariana- I believe the AI's output was mostly accurate. All the tasks for this sprint were well distributed, and everyone did a great job while maintaining good communication.

ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

Sprint Retrospective

Date: 25/10/2025

What went well?

- The first sprint was successful. Our effective sprint planning made it easier to organize and carry out the project. We maintained good communication and held daily meetings almost every day.
- We finished our work early, leaving the last week for reviewing.
- Everyone was engaged and contributed actively throughout the sprint.
- The communication among the team was great.

What went wrong?

- One of the issues we encountered was that some team members made commits containing many changes at once, instead of breaking them into smaller, separate commits.
- A few merge conflicts happened because multiple people worked on the same files.
- Some user stories were not fully clarified at the start, leading to rework.
- Some tasks took longer than expected due to underestimated complexity.

What we learned?

- This sprint taught us that everything is easier when we work as a team. We also learned how to make meaningful decisions when we don't have answers from the customer.
- We learned how to better plan and prioritize user stories during sprint planning.
- The importance of committing smaller, incremental changes to avoid merge conflicts.
- The importance of properly grooming the backlog to plan realistic sprint goals, and how sprint reviews help the team gather feedback and improve our workflow for the next sprint.

Sprint Retrospective

Date: 25/10/2025

Action items:


- Improve USLP03 implementation by establishing a direct connection between the database server and the IDE, enabling it to retrieve the necessary data directly.
- Develop a functional graphical interface for the application.

Overall Project performance:

- Comments: everything said in the sprint retrospective.

- LLM evaluation: LLM was quite effective in analyzing code and suggesting improvements. The responses were coherent, but sometimes very generic. We rated the performance as good (4).

- How do you grade your performance (0-5): 4
- How do you grade your results (0-5): 4



ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

