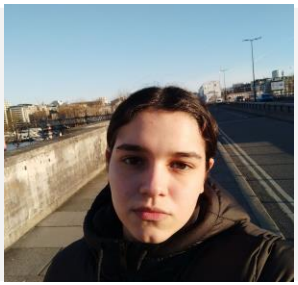
ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

LAPR3 2025/2026

[Logistics On Rails] - **SPRINT 2**

G051

Sofia Carvalho (1240898)	Mariana Moreira (1240905)	Leonor Moura (1240914)	Francisco Sá (1241341)
			

Sprint planning – Sprint 2

Planned Start Date: November 3rd

Planned End Date: November 21st

Real Start Date: November 5th

Real End Date: November 23rd

SPRINT BACKLOG		
Number of stories	22	
Number of bugs	0	
Number of tasks	33	
Number of Management Tasks (Scrum)	11	
Number of team members	Planned: 6	Actual: 6
Total planned **estimation** vs execution	Planned hours: 133 Executed hours: 125	

Sprint 2 planning

Assigned User Stories (as stated in the project assignment)	Commited? Yes / No (according to team planning)	Todo	Doing	Testing	Done	Blocked
USBD21	Yes				x	
USBD22	Yes				x	
USBD23	Yes				x	
USBD25	Yes				x	
USBD27	Yes				x	
USAC01	Yes				x	
USAC02	Yes				x	


Sprint 2 planning

Assigned User Stories (as stated in the project assignment)	Commited? Yes / No (according to team planning)	Todo	Doing	Testing	Done	Blocked
USAC03	Yes				x	
USAC04	Yes				x	
USAC05	Yes				x	
USAC06	Yes				x	
USAC07	Yes				x	
USAC08	Yes				x	
USAC09	Yes				x	
USEI06	Yes				x	


Sprint 2 planning

Assigned User Stories (as stated in the project assignment)	Commited? Yes / No (according to team planning)	Todo	Doing	Testing	Done	Blocked
USEI07	Yes				x	
USEI08	Yes				x	
USEI09	Yes				x	
USEI10	Yes				x	
USLP05	Yes				x	
USLP06	Yes				x	
USLP07	Yes					x

Work assigned by team member

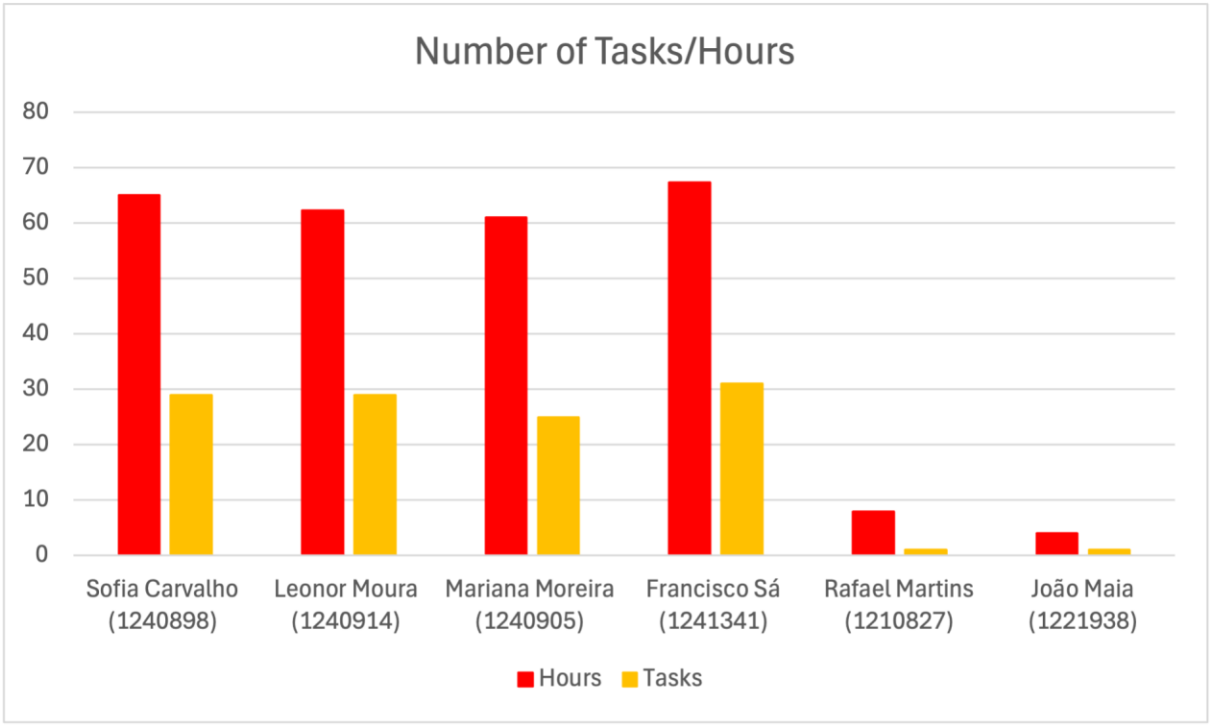

Work assigned by type (component)

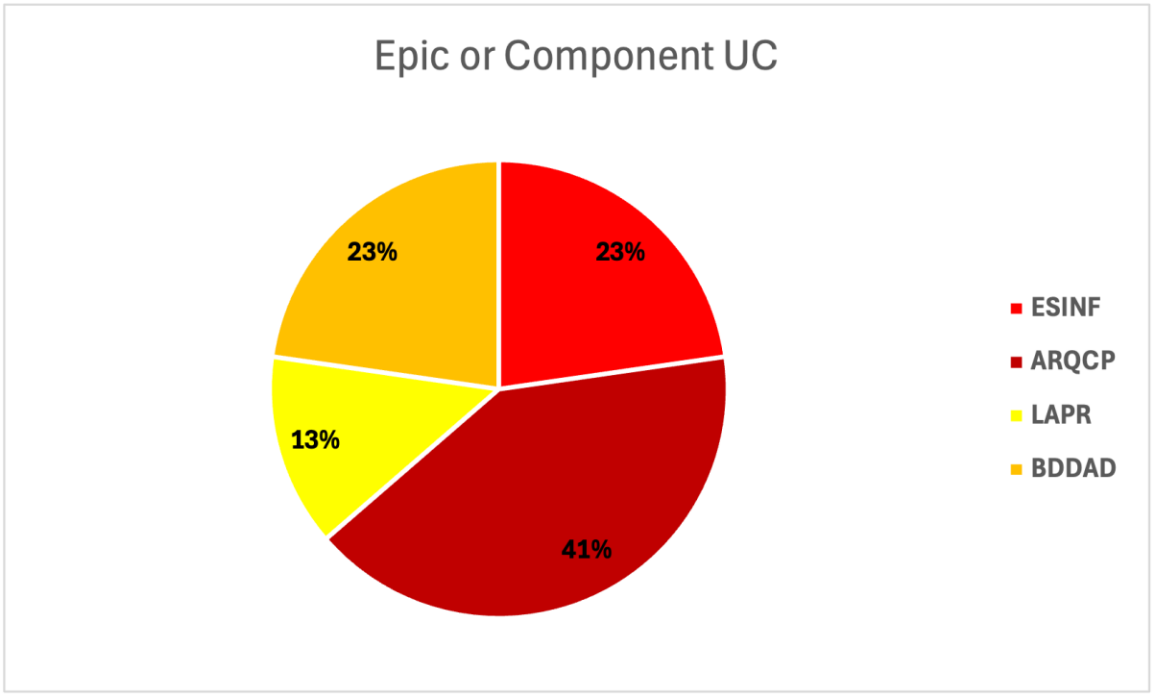

Issues / Assumptions / unanswered questions

Description	Responsible	Date / sprint	Related issue / item in Git
For the user story USLP07 - As Freight Manager, I want to use a scheduler that allows me to dispatch a list of trains. Each train has an associated route that can be simple or complex. There are still some scenarios for the crossing operations that we want to improve.	All	Sprint 2	#83

Daily Meetings

Date (of the meeting)	Place / duration	Team member 1	Team member 2	Team member 3	Team member 4
29/10/2025	Class / 15 min	x	x	x	x
30/10/2025	Class / 15 min	x	x	x	x
05/11/2025	Class / 15 min	x	x	x	x
06/11/2025	Class / 15 min	x	x	x	x
07/11/2025	Class / 15 min	x	x	x	x
11/11/2025	Class / 15 min	x	x	x	x
12/11/2025	Class / 15 min	x	x	x	x
13/11/2025	Class / 15 min	x	x	x	x
14/11/2025	Class / 15 min	x	x	x	x

Daily Meetings

Date (of the meeting)	Place / duration	Team member 1	Team member 2	Team member 3	Team member 4
19/11/2025	Class / 15 min	x	x	x	x
20/11/2025	Class / 15 min	x	x	x	x
21/11/2025	Class / 15 min	x	x	x	x

LLM performance assessment - Input (use ChatGPT or Copilot)

Source file (attach the file you have used):
The file is stored on the repository, following this path
sem-3-pi-25-26-g051-repo/Project/Scrum/Sprint2/SprintReview/Team Performance.pdf

Input (write down the prompt you used to ask for the performance assessment):

> Let me know what you think about my team's performance in this review. You can find each team member's time/task schedule here for more effective feedback.

LLM performance assessment - Output

Output file (attach the complete file extracted from the A.I. tool):

https://chatgpt.com/c/69232b23-03ec-832f-8672-3d762ee11820

Output (write one line per team member):

Francisco Sá (1241341) - Consistent and Reliable- Shows strong technical engagement and situational awareness
Sofia Carvalho (1240898) - Clear Communicator - Demonstrates strong reliability and awareness of group work
Leonor Moura (1240914) - Optimistic and Organized - Shows awareness of future priorities
Mariana Moreira (1240905) - Consistent and steady progress - Reinforces team communication and collaboration

LLM performance assessment – Critical Insight

Team Members' Opinion about the A.I. output

Francisco – The AI's assessment is almost entirely accurate. Our sprint was well balanced overall, with the exception of Rafael's workload, since he only had ESINF tasks—which is understandable.
Sofia – Overall, I believe the team's work distribution and performance were very balanced. Everyone contributed consistently and maintained a similar level of effort and productivity.
Leonor – I think the AI's analysis is generally correct. The team performed very well, the workload was evenly distributed, and everyone contributed meaningfully to the sprint's success.
Mariana – I find the AI's output largely accurate. The tasks for this sprint were well distributed, and the whole team did a great job while maintaining strong communication.

Improvement Suggestion from LLM:

Improve detail of daily tasks and team reflection

ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

Sprint Retrospective

Date:

What went well?

- The sprint was successful, we had great communication;
- We finished all the user stories requested for this sprint;
- We were able to review our work with plenty of time;
- All team members were active trhoughout the sprint.

What went wrong?

- There were still some merge conflicts, but the number has improved from the last sprint;
- Some tasks were started later than planned due to ambiguity in priorities, which caused slight delays in progress;
- Some user stories expanded in scope during development;
- Some tasks were more complicated then what we thought.

What we learned?

- The sprint is easier when everyone helps and communicates with each other;
- We recognized the importance of committing smaller, incremental changes to reduce the risk of merge conflicts;
- We improved our ability to plan and prioritize user stories;
- We improved our ability to adapt when priorities shifted

Sprint Retrospective

Date: 23/11/2025

Action items:


- Improve crossing feature developed on USLP07;
- Develop a functional graphical interface for the application for the last sprint of the project.

Overall Project Performance:

LLM evaluation: The LLM was helpful in reviewing our performance and providing optimization ideas. While the answers were usually clear, they occasionally lacked specificity. We assigned it a performance rating of 4.

Team evaluation: As a team, we feel like we work very well together. The project developed meets ou expectations. We would grade ourselves with a 5, on a scale from 1 to 5.

Team feeling: We are feeling that the next sprint is going to be as succesfull as the previous ones.



Checklist Sprint 2

Item	Objective
US detailed in the Backlog	Mandatory
Start **Sprint 2**	Mandatory
Priorities	Mandatory
Estimate US **(hours)**	Mandatory
Create Subtasks	Mandatory
Customize board	Mandatory
Integrate with Git	Mandatory
Create milestones	Discretionary

Item	Objective
Create Sprint planning Task **Sprint 2**	Mandatory
Create tasks for Daily meetings (3 per week avg)	Mandatory
Update US and task status on board	Mandatory
Submit working hours	Mandatory
Include outstanding items from Sprint 1	Discretionary
Include outstanding items from Retrospective	Mandatory
Estimate using Planning Poker	Mandatory

ISEP INSTITUTO SUPERIOR DE ENGENHARIA DO PORTO

